

Work Order ID 157393

Tuesday, February 21, 2017 1:12:16 PM

157393

Page 1

Item ID: D119-796-151

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: FWD Crosstube Installation with Step (no hardware)

Start Date: 2/24/2017

Start Qty: 1.00

1

Cust Item ID:

Required Date: 3/22/2017

Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan:

DAS
21
9-89

Date:

FEB 27 2017

Tooling:

Date:

QC:

Date:

SPC (Y/N):

Date:

Run Start ***NR1***Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D119-796-151	D

110

Document Control

0.00

110

DC

Memo

0.00

Doc.Control -USB or Paperwork

Photocopy bluefile and create labels as per PPP D119-796-151 chg 004

N/A

120

Pick Kit

0.00

120

Packaging

Packaging

Memo

0.00

Packaging

1

DAS
41
9-89

JUN 06 2017

130

Crosstubes

0.00

130

Crosstubes

Memo

0.11

Crosstubes

1- Install step and clamp with the proper position per dwg D119-796-151

1

DAS
41
9-89

JUN 06 2017

Torque all clamps to 50 IN-LBS max.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

Work Order ID 157393


Tuesday, February 21, 2017 1:12:16 PM

157393

Page 2

Item ID: D119-796-151 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: FWD Crosstube Installation with Step (no hardware)
 Start Date: 2/24/2017 Start Qty: 1.00 ***1*** Cust Item ID:
 Required Date: 3/22/2017 Req'd Qty: 1.00 ***1*** Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
140 *140* QC Quality Control	QC5- Inspect part completeness to step on W/O Memo ***RE-CHECK TORQUE ON CLAMP AS PER DWG.*** ***VERIFY BY <u>157393</u> ³⁸ ₉₋₈₈ BATCH # TO MATCH W/O ***VERIFY BY <u>157393</u> ³⁸ ₉₋₈₈ PART # TO MATCH W/O <u>157393</u> ³⁸ ₉₋₈₈	0.00 0.00				1			DAS 38 9-88 JUN 06 2017
150 *150* Packaging Packaging	Packaging Memo Identify and pack for shipping as per PPP D119-796-151 Au1	0.00 0.00				1			DAS 41 9-88 JUN 06 2017
160 *160* QC Quality Control	QC21- Final Inspection - Work Order Release Memo	0.00 0.02							17/6/17 



JUN 06 2017

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor Approval Verification		
			QC / QA Coordinator Approval		
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Picklist Print

Tuesday, February 21, 2017 1:12:19 PM

Page 1

Work Order ID: 157393

157393

Parent Item: D119-796-151

D119-796-151

Parent Item Name: FWD Crosstube Installation with Step (no hardware)

Start Date: 2/24/2017

Required Date: 3/22/2017

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP REV:A 14.09.09 NEW ISSUE DD VERF:JLM IPP
REV:B 14.11.19 AS PER REV.C DD VERF:JLM IPP REV:C
14.12.09 AS PER REV.PC6 DD VERF:JLM IPP REV:D 15-02-11
AS PER REV D JLM VERIFIED BY:DD

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D119-796-141		Manufactured	No			120	Each	0.0000	1	1	DAS 41 9-89		
D119-796-141					157378				**	1		MAY 26 2017	
FWD Crosstube Installation without Step (no hardware)													
D5123-3		Manufactured	No			120	Each	410.0000	4	4	DAS 41 9-89		
D5123-3									**			MAY 26 2017	
Clamp Cushion													
				<u>Location</u>		<u>Loc Qty</u>	<u>Loc Code</u>						
				LG052		400							
				153233		400		4					
				LG055		10							
				152482		10							
D5149-041		Manufactured	No			120	Each	7.0000	2	2	DAS 41 9-89		
D5149-041									**			JUN 06 2017	
Fwd Step Base Assembly													
				<u>Location</u>		<u>Loc Qty</u>	<u>Loc Code</u>						
				LG055		7							
				156586		1		2					
				156587		6							

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
2011 18 08 0								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : _____			

Picklist Print

Tuesday, February 21, 2017 1:12:19 PM

Page 2

Work Order ID: 157393

157393

Parent Item: D119-796-151

D119-796-151

Parent Item Name: FWD Crosstube Installation with Step (no hardware)

Start Date: 2/24/2017

Required Date: 3/22/2017

Start Qty: 1.00

Required Qty: 1.00

MS21920-22

Purchased

No

120

Each

74.0000

4

4

MS21920-22

Clamp

DAS
41
9-89

MAY 26 2017

Location

Loc Qty

Loc Code

LG050

50

M136768

50

LG056

24

M135603

24

4

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____


Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. 2A	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : 1A	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor Approval Verification		
			QC / QA Coordinator Approval		
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐				
OTHER : ☐					


ITEM	QTY	P/N	DESCRIPTION
	X	D119-796-151	XTUBE ASSY (AW119 MKII FWD)
1	1	D119-796-141	XTUBE ASSY (AW119 MKII FWD)
2	4	D5123-3	CUSHION
3	2	D5149-041	FWD STEP ASSEMBLY
4	4	MS21920-22	CLAMP

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 157393 HLT
1702-27

D119-796-141 XTUBE
BENDING PLANE

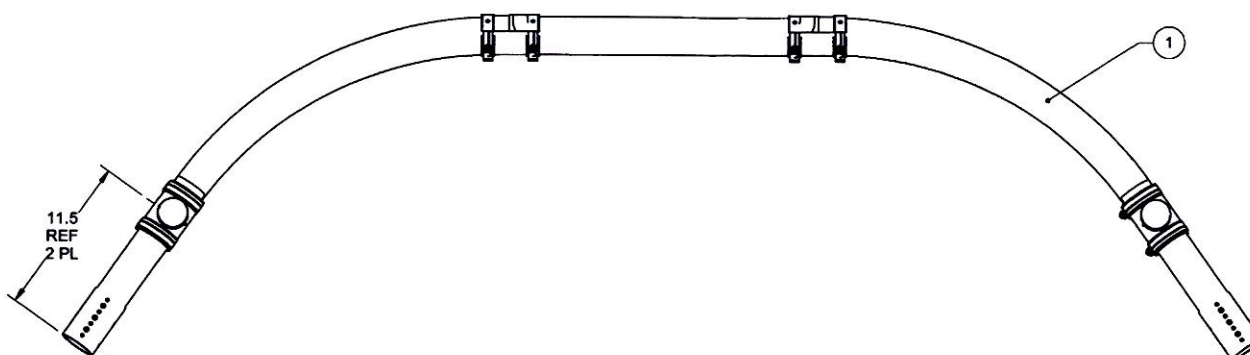

D119-796-151 XTUBE ASSY (AW119 MKII FWD)

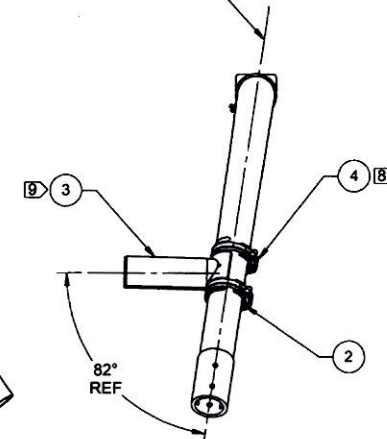

RELEASED

2015 FEB 09

ECN 15-516 9

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 METHOD 6.5
- 7) WEIGHT: 19.87 lbs
- 8) TORQUE MS21920-22 CLAMPS TO 50 IN-LBS MAX
- 9) LOCATE STEP USING POST FITTING ON CROSSTUBE

D	D5123-3 CLAMP CUSHION WAS D5123-9 CLAMP CUSHION, MS21920-22 WAS -24.	AP	15.01.19
C	RE-DESIGN STEP INSTALLATION	DB	14.11.24
B	D5149-043 WAS D5149-041, AN4C8A WAS AN4C10A, D2274 WAS D5153-1	AP	14.11.04
A	NEW ISSUE	AP	14.09.03
REV.	DESCRIPTION	BY	DATE
DESIGN	AP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	DB	DRAWING NO. D119-796-151	
MFG. APPR.	JLM		
APPROVED	HS	TITLE XTUBE ASSY (AW119 MKII FWD)	
DE APPR.	DS		
DATE	15.01.19	REV. D SHEET 1 OF 1 SCALE NTS	

COPYRIGHT © 2014 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS
NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT
WRITTEN PERMISSION FROM DART AEROSPACE LTD.
